



Interconnection Queue Status Update

June 2023 IPS

Jeriotte Ragsdale

Sr. Engineer

Interconnection Planning Projects

Priorities in order:

1. Manage AD2 and priors
 - AD2 takes us to July time period fully executed
2. Develop tools and processes for new process and transition
3. Issue AE1 through AG1 final agreements until July 7, 2023
 - Issued in queue priority and project readiness

July 10th
 Target Transition Start

2023

Jan. – Mar.

Apr. – Jun.

Jul. – Aug.

Sept. – Dec.

- **PJM Primary Focus** – Issuing AD1/AD2 ISAs
- **AE1-AG1** - Continue to issue agreements as analysis/timing/priority permits


- **Execution** of AD1/AD2 ISAs
- **AE1-AG1** - Continue to issue agreements as analysis/timing/priority permits

(60-day period from Transition Start Date)


- Eligibility Period:** AE1-AG1 not in receipt of final agreements prior to transition have 60 days to provide:
- \$4,000/MW readiness deposit
 - Site control for generating site for one year from transition date

- PJM **finalize review** deposits/site control and determine cohort of projects to move forward
- PJM will **update models** based on cohort moving forward into transition
- **Retool 1:** Retool analysis to determine Fast Track vs. TC1 projects.
- **Retool 2:** Retool Fast Track with TC1 projects removed from model.
- **Note:** *LF/SC/Stability models all need to be updated/retool ran prior to being able to issue final agreements in Fast Track.*

FINAL AGREEMENTS ISSUED

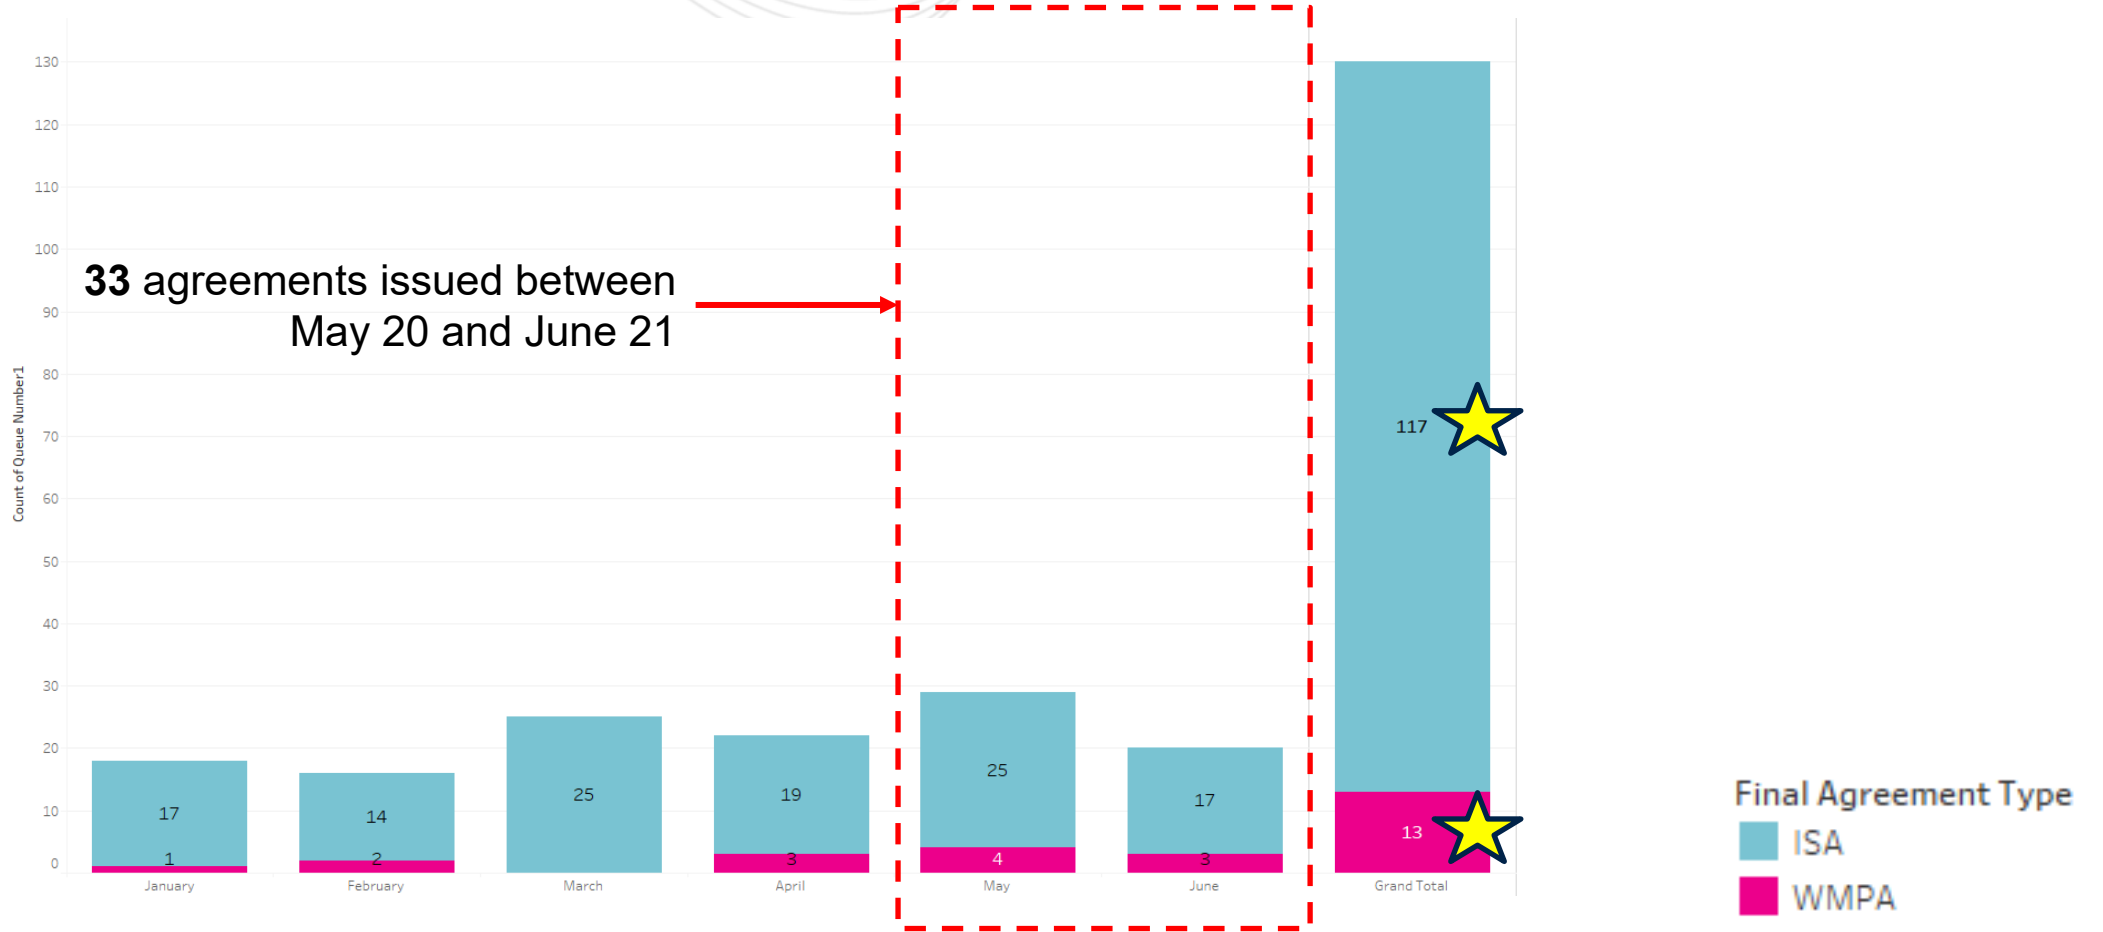

REMAINING PROJECTS IN AE1-AG1

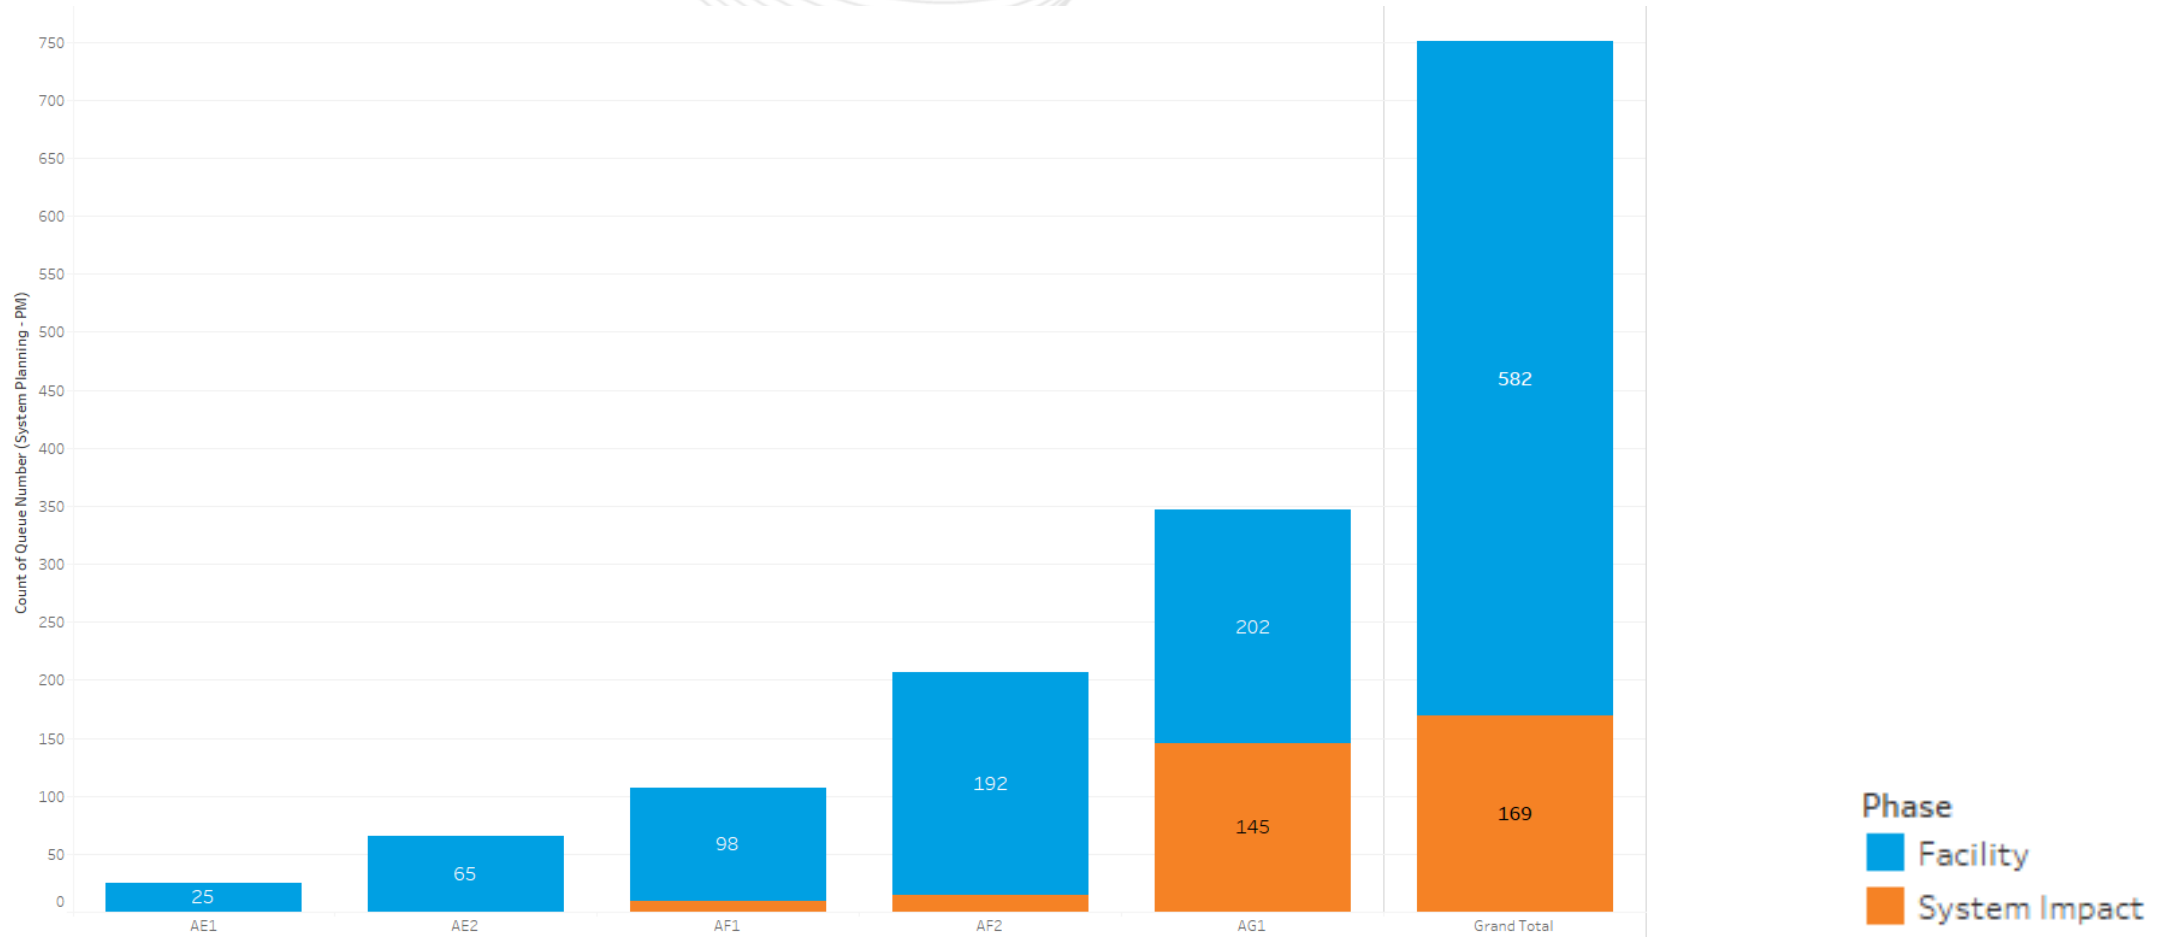

- **Analysis Complete**
 - Load flow, Short Circuit, Stability Analysis is complete and any needed reinforcements
 - Cost allocation clarity for network upgrades
 - i.e. either first to cause, or next up in stack up with prior position securing
- **Facility Study Complete**
 - Need TO-provided facilities study for physical interconnection and reliability driven network upgrades
- **All Inputs Submitted by Customer and TO Review Complete**
 - Completed input agreement forms with updated site maps and GPS coordinates marked and submitted to PM
 - TO review and comments provided, negotiated, and incorporated into draft agreements

NO MORE CHANGES BEING ACCEPTED FOR MATERIAL MODIFICATION REVIEW!

Reduction requests within Tariff limits: Accepted up to **June 29th COB**, only if Queue Point is updated accordingly.

For Change Requests that were submitted by May 15th:

PJM completed all Material Modification reviews on June 16th:

- **If Change Request was found NOT material** – Queue Point must be updated by **June 29th** in order to be captured in the Transition Retool.
- **If Change Requests was found to be material** – If you still want the reduction, Queue Point must be updated by **June 29th** and project will slide to next queue. Otherwise, no changes will be made to the original project for the Transition Retool. POI and fuel changes found to be material will not be allowed.

Presenter:

Jeriotte Ragsdale, Sr. Engineer,
Interconnection Planning Projects

Jeriotte.Ragsdale@pjm.com



Member Hotline

(610) 666 – 8980

(866) 400 – 8980

custsvc@pjm.com
